



FRAP-
21.02

NORA EZ Infrastructure Project Highlight Report

Project Name:	NORA EZ Infrastructure	Project Manager:	Mark Fuller	Project Sponsor:	Matthew Henry	Report covers period of:	Q2 2024-25
Capital Code:	C8501-4	Client Dept:	-	Lead Designer:	NCC		
Project Code:	P-21.02	End User (if applicable):	-	Cost Consultant:	NCC		
				Contractor on Site:	Octavius		

Management Summary

	1. Overall Status	2.1 Risks	2.2. Issues	3. Financials	4. Timelines	5. Resources
This Report	R	G	A	R	R	G
Last Report	R	R	A	R	R	G

Project Definition

Project Stage: RIBA Stage 5: Construction

Objectives: Development of secondary road infrastructure and services on the Nar Ouse Enterprise Zone

Scope: Construction of secondary road infrastructure and services on eastern side of Enterprise Zone (excludes western side of site and Active Travel Hub)

1. Overall Status (high-level summary)

The overall status is Red due to

- NCC reporting significant overspend due to delays caused by AWS, UKPN, Cadent and Phosphor Gypsum removal.

1.1 Decisions required by the Officer Major Projects Board

- No Decisions required.

1.2 Achievements during this period

- Works substantially completed 06.09.24 and contractor demobilised from site w/c 30.09.24

2. Risks and Issues

2.1 Key Risks [all red and increasing amber]

A risk is something that may happen

Risk ID (3/22)	Risk Title	Description	RAG Status	Risk Category	Mitigation	Dated Comments
			G			

2.2 Key Issues [all red and increasing amber]

An issue is something that has happened

Issue ID (3/3)	Issue Title	Description	RAG Status	Issue Type	Resolution Plan	Dated Comments
1/2	NCC reporting contract overspend	A number of issues causing overspend, AWS, Cadent, UKPN and requirement to remove Phosphor Gypsum	R	Cost	Currently in dialogue with senior officers at NCC. Secured additional funding via Cabinet to deal with Phosphor Gypsum. Seeking independent Legal advice.	14.10.24 Ongoing – Legal engaged.
2/3	Anglian Water Services	Delays in signing off drainage design and other AWS related matters	A	Time and cost	Active engagement and dialogue with AWS to secure approvals. Outstanding issues being closed off – minimal items remain outstanding – but formal written consent not signed off.	14.10.24 Ongoing
3/3	Cadent approval	Approval of protection slab over high pressure gas main by Cadent	A	Time and cost	NCC actively engaged with Cadent. Live issue that NCC / Octavius are actively engaged with Cadent to resolve.	14.10.24 Ongoing – Cadent verbally agreed happy with slab design - contractor will return to site to complete these works.

Note: further detail on Project Risks and Issues can be found in the Risks and Issues Log.

3.1 Project Financials

Financial information not available.


3.2 Project Contingency and Change Control

Change Ref	Description	Cost Impact	Programme Impact	Other Impact	RAG Status	Approval given by	Date of change
	N/A						

3.3 Financial Commentary

Financials RAG is currently Red on the basis of NCC reporting potential overspend due to continued delays to contract completion, impact of AWS, UKPN, Cadent issues and Phosphor Gypsum removal.

4. Timelines – High Level Milestones

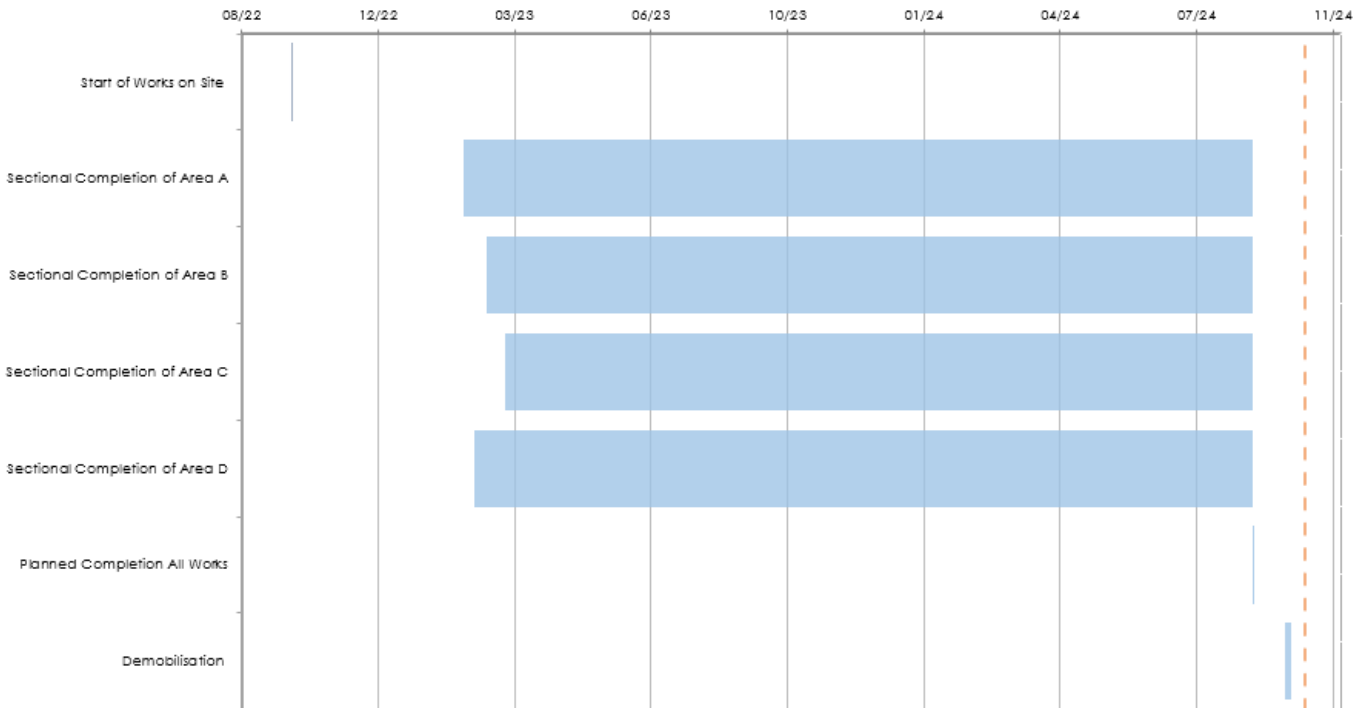

4.1 Timelines Commentary

Timelines RAG status is Red due to significant delays in infrastructure delivery against the original programme, largely due to delays in AWS sign off of drainage designs and on going negotiations with Cadent.

5. Resources Commentary

Resources RAG status is currently Green. Project support – vacant posts x2 in Property Team limited impact on this project.

6. Communications and Engagement

Communications Team advised of current programme and of Phase I and Phase II status. No wider communication or engagement at this time.

7. Outputs and Outcomes

7.1 Outputs		
Description	Target	Notes
Secondary road infrastructure to Eastern side of the Enterprise Zone		
Site wide earthworks for the Eastern side of the Enterprise Zone		

7.2 Outcomes	
Description	Notes
Provides physical access to Phase 1, Phase 2 and wider Enterprise Zone development allowing disposal and development of plots	
New development and business relocation to Enterprise Zone	
New jobs and employment opportunities	

8. Other Matters	
Item	Comment
General stage progress	RIBA 5 – Construction
Procurement progress	Complete
Proposed form of contract (e.g. JCT, NEC, Traditional, D&B)	NEC 4
Proposed route to market (e.g. IOTT, Framework ie DPS, HPCS, LCP)	Framework – Eastern Highways Alliance
Surveys Status	Complete
Statutory updates	Delays as a result of AWS and Cadent.
Health and safety	No issues reported this reporting period
Local schemes / dependencies	Phase I Spec Build Units Wider disposal and development of site
Marketing of sites	Activity on site is generating interest – will engage with interested parties when there is more certainty around delivery – and commence formal marketing at the same time.

9. Approved Documents								
	OBC [RIBA 0 Approval]	Client Brief [RIBA 1 Initiation]	Resource Brief	PID [RIBA 1 Gateway]	PID Update [RIBA 2 Gateway]	PID Update [RIBA 3 Gateway]	PID Update [pre tender]	Final PID [post tender]
Status:	✓	✓	✓	✓	✓	✓	✓	✓
Date Approved:	24.09.2019							24.09.2019
Approved by:	Cabinet	Nar Ouse Steering Group		Nar Ouse Steering Group	Nar Ouse Steering Group	Nar Ouse Steering Group	Nar Ouse Steering Group	Cabinet
Latest approved document: Final PID, Cabinet September 2019								

Spend - Budget Variance (inc. contingency)	
R	More than 10% over or under budget
A	Between 5% & 10% over or under budget
G	Within 5% of budget or less than £10k

Milestone Delivery RAG Status	
R	13 weeks or more behind the critical path
A	4 to 12 weeks behind the critical path
G	4 weeks or less behind the critical path

Risks & Issues RAG Status	
R	Needs immediate attention
A	Needs attention before next project review
G	Can be managed
